



Using portable battery systems to commission transformers

ZENOBĚ

H2 2025

[Zenobē.com](https://zenobe.com)





Executive summary

- + Power System CAPEX projects can take advantage of portable generation to commission electrical equipment before a grid connection is available
- + Commissioning such equipment involves energising transformers which traditionally require large generator systems to provide inrush currents
- + Zenobē have used commissioning experience and portable power expertise to develop an alternative solution using a mobile BESS¹ (Powerskid) to execute a controlled ramp up of the voltage and limit the inrush currents, reducing generator size requirements by up to 30x
- + Further savings are made by using the Powerskids to handle load step changes during commissioning to improve generator operating efficiency
- + Case Study
 - + 300MW BESS project with 102 pairs of MV Tx was commissioned ahead of grid connection in summer 2025
 - + For the 12-week Hot Commissioning process, Zenobē Portable Power provided 2 x Powerskids, 2 x 300kVA generators and associated equipment and services to enable a full energisation and ongoing commissioning program as a hybrid system
 - + Zenobe Portable Power worked closely with project team before and during the project to develop and adapt operation strategy throughout, ensuring it meets commissioning requirements at each stage while optimising fuel usage
 - + Hot Commissioning savings achieved 28% of c.£1m expected cost from a traditional generator solution
 - + **Total cost for portable power solution to the example project was 28% lower than benchmark solution (c.£1m expected cost from a traditional generator solution) including fuel savings of 260,000 litres and 707 tCO₂**

¹ BESS: Battery Energy Storage System



Case Study: Kilmarnock South 300MW/600MWh BESS

Problem	Traditional Solution	Portable Power Solution	Benefits of PP Solution
<p>Transformer Energisation</p> <ul style="list-style-type: none">Energising transformers at nominal voltage results in a significant inrush current, requiring a large power supply to enable itKilmarnock South has over 100 MV Transformer pairs that need to be energised during hot commissioning	<p>Generator Size</p> <ul style="list-style-type: none">Each pair of Transformers on Kilmarnock would be commissioned one at a time at nominal voltage without a grid available.For a 2MVA Tx, 3.5MVA of generator capacity is required to manage the active and reactive power demands of the inrush current	<p>Voltage Ramp Up</p> <ul style="list-style-type: none">Instead of energising at nominal voltage, a Powerskid inverter executes a controlled ramps up the nominal voltage on the LV side of the Tx, inrush current is reduced by a factor of 30x only a small generator required to supply ongoing energy requirementsAfter the first pairs of site inverters are commissioned, they can be used to support the inrush current from the energisation of the remaining skids on site which happens at nominal voltage	<ul style="list-style-type: none">Reduction of generator and additional equipment hire and transport costs -> Savings c.50% on hire costsFuel consumption reduction due to correct generator sizing and running at optimum loading -> Fuel savings c.35%, 262,000ltrs and 707tCO2Total reduction in costs for temporary power solution for hot commissioning Kilmarnock -> c.28% of temporary power for commissioning costs
<p>Inverter Commissioning Step Changes</p> <ul style="list-style-type: none">After initial energisation, commissioning required step changes of the order of 100kWThe steps prevented the generators working in a load on demand system, as they would trip before the system could respond and support	<p>Fixed Export Generators</p> <ul style="list-style-type: none">Generators run in fixed export mode with a load bank, so the step changes did not cause trippingThis resulted in large amounts of fuel being burned and dissipated in the load bank	<p>Batteries Supporting Generators</p> <ul style="list-style-type: none">Using mobile batteries mean that they can respond easily to step changes in the load, protecting the generators and mitigating the risk of trippingGenerators are still used to provide the energy but only run to supply energy used for commissioning rather than into a load bank	



Solution comparison - equipment

Generator-only solution

- + Consists of 3.75MVA of generator capacity to manage Tx energisation. A diagram of the proposed solution is in Fig 1, which had weekly hire costs of £15k+
- + Generators were expected run in non-efficient strategy to ensure they could handle the variability in load throughout the commissioning process

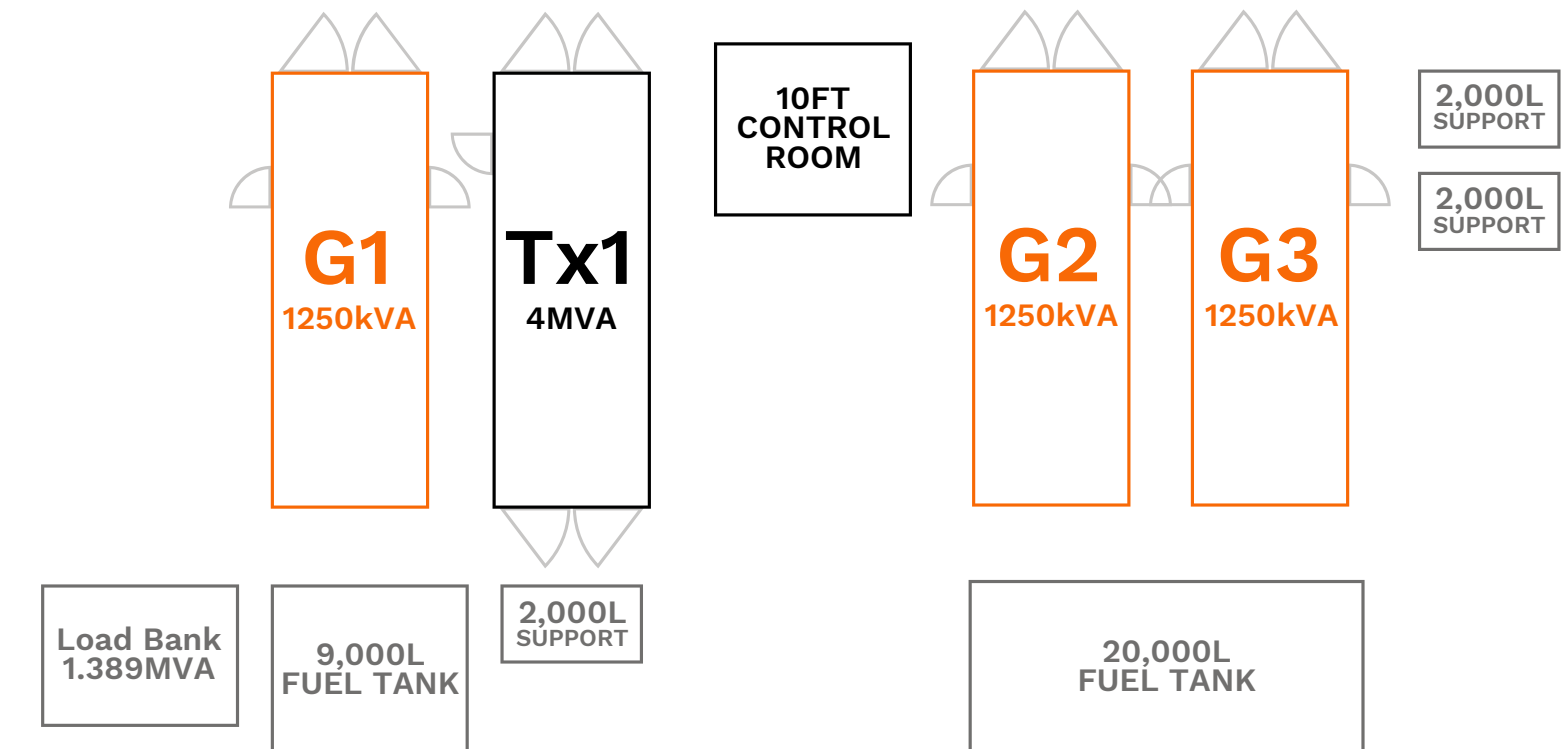


Fig 1: Gen Only Solution proposed by generator supplier made up of 3.75MVA Generators, 1.4MVA load bank and corresponding fuel and control equipment

Hybrid Solution

- + Using Powerskids to reduce the inrush current during energisation reduces the required generator capacity by a factor of six to 600kVA. New solution is illustrated in Fig 2.
- + The Powerskid inverters will handle the load variability during commissioning and enable the generators to only run when needed in their most efficient manner
- + Generator capacity was increased in project to provide more energy to site at a later stage
- + Battery and generator operating strategy was adjusted through commissioning project to ensure performance and maximise fuel savings

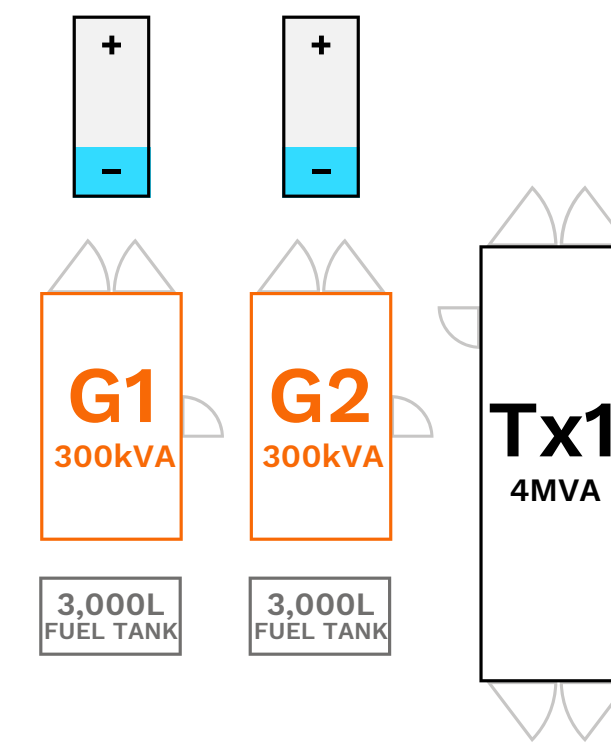


Fig 2: Hybrid Solution developed by Zenobē Portable Power with project Construction team, made up of 600kVA of generators with 2 x 100kW/150kWh Powerskids



Fig 3: Real Hybrid Solution in operation on site



Technical Description

- The magnetisation process is managed by using the PowerSkid to execute a controlled ramp of both the current and voltage of the connected transformers.
- The voltage steps were automated at 5% increments and were only incremented if the current draw remained below a current limit threshold. Test results illustrating the approach are shown in Figure 4 below.
- This controlled ramp capability and overall microgrid management techniques are utilised throughout the commissioning process as requirements from the hybrid portable power supply vary

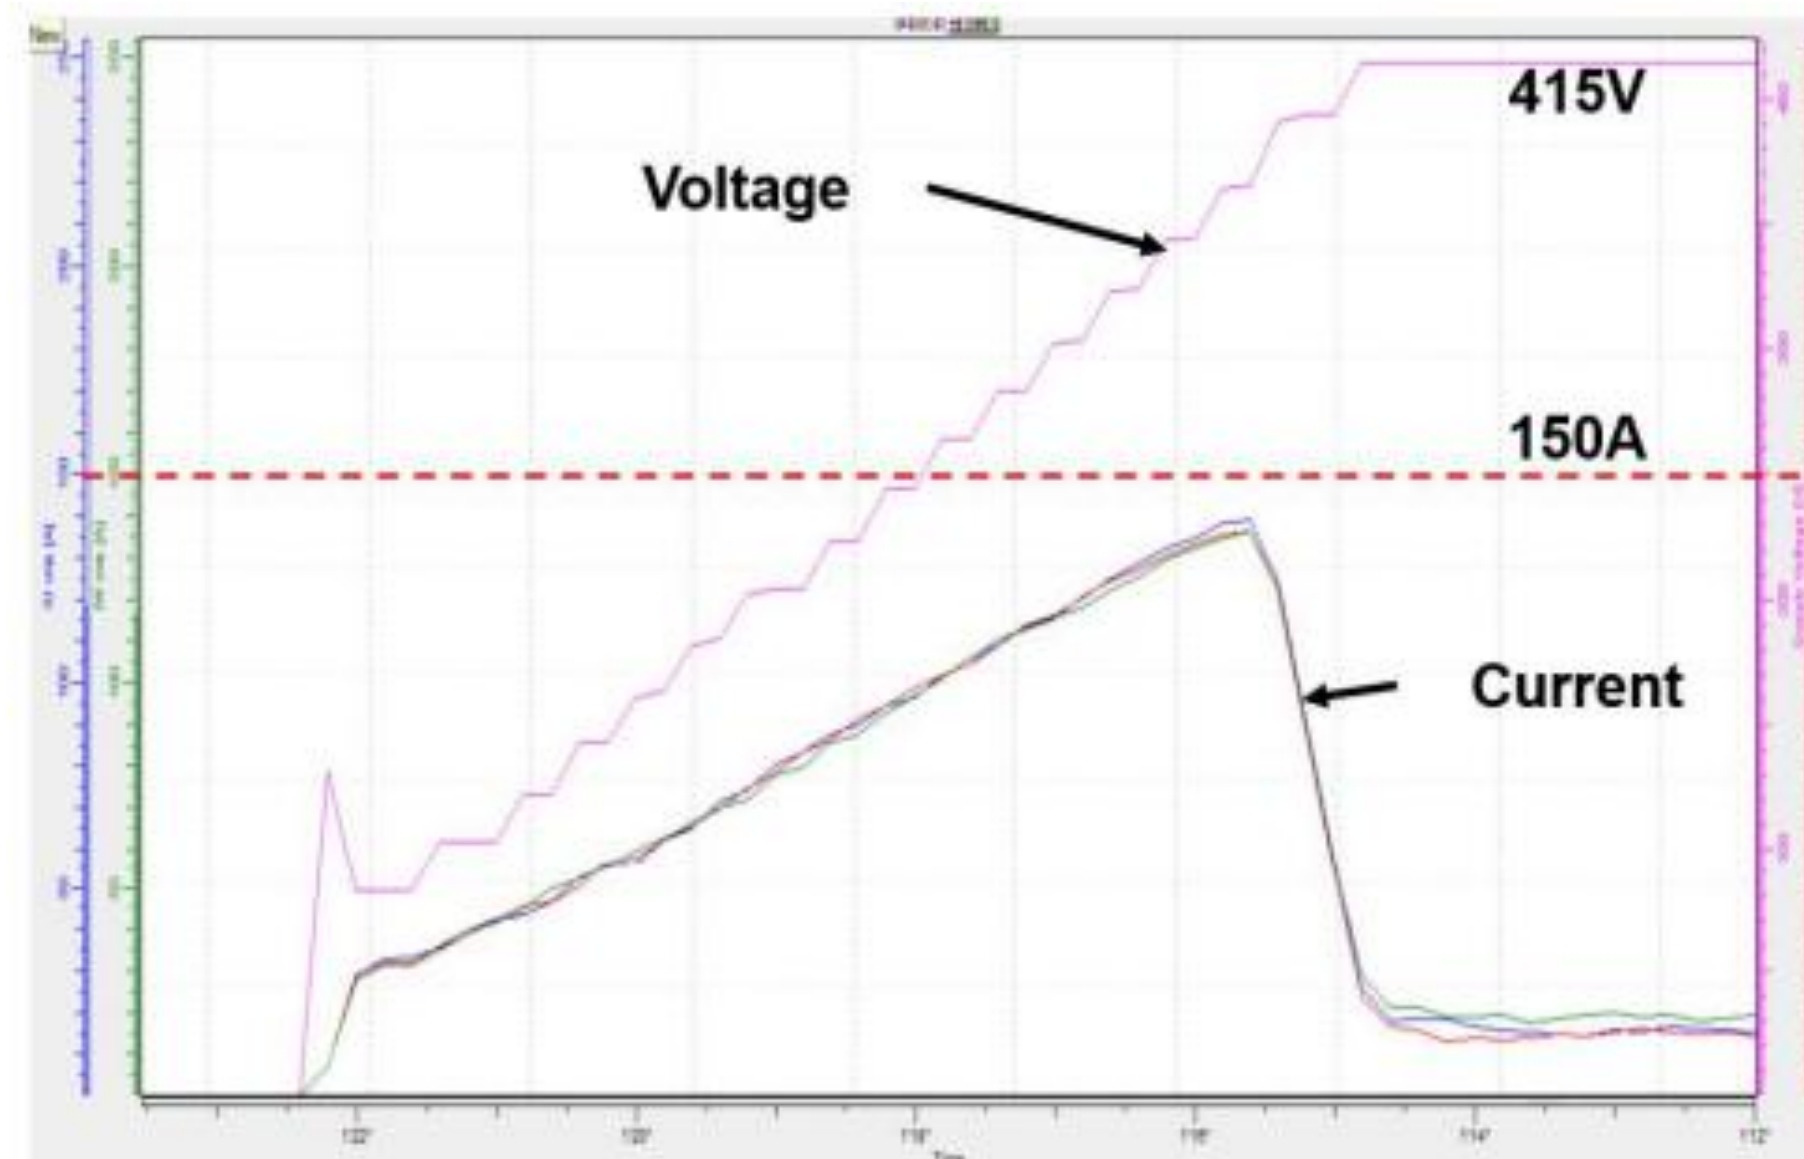


Fig 4: Plot showing voltage and current during ramped magnetisation process



Commission smarter with **battery**
storage. Reach out to learn more.

ZENOBĒ

portablepower@zenobe.com



Robert Long
Head of Portable Power
robert.long@zenobe.com



Chris Slevin
Senior BD Associate – Portable Power
chris.slevin@zenobe.com



Disclaimer

THIS PRESENTATION HAS BEEN PREPARED FOR INFORMATIONAL PURPOSES ONLY. ALTHOUGH THE INFORMATION CONTAINED IN THIS PRESENTATION HAS BEEN OBTAINED FROM SOURCES WHICH ZENOBĒ ENERGY BELIEVE TO BE RELIABLE, IT HAS NOT BEEN INDEPENDENTLY VERIFIED AND NO REPRESENTATION OR WARRANTY, EXPRESS OR IMPLIED, IS MADE AND NO RESPONSIBILITY IS OR WILL BE ACCEPTED BY US AS TO OR IN RELATION TO THE ACCURACY, RELIABILITY OR COMPLETENESS OF ANY SUCH INFORMATION.

THE INFORMATION AND OPINIONS CONTAINED IN THIS PRESENTATION ARE NOT INTENDED TO BE THE SOLE BASIS UPON WHICH THE IMPLEMENTATION OF THE OPERATION CONTEMPLATED HEREIN (THE “OPERATION”) CAN BE DECIDED. IT IS THEREFORE ADVISABLE FOR THE RECIPIENT(S) TO MAKE ITS/THEIR OWN JUDGEMENT AND ASSESSMENT OF THE INFORMATION AND THE OPERATION CONTAINED IN THIS PRESENTATION.

OPINIONS EXPRESSED HEREIN REFLECT OUR JUDGEMENT AS OF THE DATE OF THIS PRESENTATION AND MAY BE SUBJECT TO CHANGE WITHOUT NOTICE IF ZENOBĒ ENERGY BECOME AWARE OF ANY INFORMATION, WHETHER SPECIFIC TO THE OPERATION OR GENERAL, WHICH MAY HAVE A MATERIAL IMPACT ON ANY SUCH OPINIONS. ZENOBĒ ENERGY WILL NOT BE RESPONSIBLE FOR ANY CONSEQUENCES RESULTING FROM THE USE OF THIS PRESENTATION AS WELL AS THE RELIANCE UPON ANY OPINION OR STATEMENT CONTAINED HEREIN OR FOR ANY OMISSION.

THIS PRESENTATION IS CONFIDENTIAL AND MAY NOT BE REPRODUCED (IN WHOLE OR IN PART) NOR SUMMARISED OR DISTRIBUTED WITHOUT OUR PRIOR WRITTEN PERMISSION. THE RECIPIENT(S) OF THIS REPORT AGREE(S) TO KEEP ITS CONTENT STRICTLY CONFIDENTIAL AND UNDERTAKE(S) NOT TO DISCLOSE THE INFORMATION CONTAINED HEREIN TO ANY PERSON OTHER THAN THOSE OF ITS/THEIR EMPLOYEES WHO STRICTLY NEED ACCESS TO IT FOR THE PURPOSE OF THE OPERATION
